

Work Order ID 142660

142660

Page 1

Monday, March 21, 2016 8:40:18 AM

Item ID: D5152-1 Accept *N900040100* Setup Start *NS1*
 Revision ID: Stop *NS2*
 Item Name: Fwd Post Mount
 Start Date: 3/22/2016 Start Qty: 20.00 *20* Cust Item ID:
 Required Date: 3/30/2016 Req'd Qty: 20.00 *20* Customer:

Reference:
 Approvals: Process Plan: W Date: _____ Tooling: _____ Date: _____ Run Start *NR1*
 QC: _____ Date: _____ SPC (Y/N): _____ Date: _____ Stop *NR2*

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
Draw Nbr	Revision Nbr								
D5152	B								

105 0.00
 105
 Purchasing
 Purchasing
 Memo
 ISSUE PO 31764
 CUT PER DRWG D5152 REV.B
 20 MAR 21 2016
 DAS 13
 9-89

115 Receive & Inspect for Damage & Mat'l Certs 0.00
 115
 Packaging
 Packaging
 Memo
 20 x 50/6-04-7
 DAS 38
 9-89

125 QC5- Inspect part completeness to step on W/O 0.00
 125
 QC
 Quality Control
 Memo
 20
 DAS 38
 9-89
 APR 08 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐																																																											
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval																																																							
Description Work Order Deviation				Disposition				Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval																																																							
Root Cause		FAULT CATEGORY																																																													
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐	Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐	Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐	Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐	Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐	Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐	Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐	Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐	LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐	Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐	Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____	
Misidentified ☐	Past Due ☐																																																														

1 42660

Monday, March 21, 2016 8:40:18 AM

N900040100

Setup Start *NS1*

Stop *NS2*

20

Cust Item ID:

20

Customer:

Reference:

Run Start *NR1*

Stop ***NR2***

QC: _____ **Date:** _____ **SPC (Y/N):** _____ **Date:** _____

134

0.00

134

Small Fab

Memo

0.04

Small Fab

FROM ON MANUAL ROLLER OR ON BRAKE AS PER DWG

**DAS
30
9-89**

APR 12 2016

136

QC5- Inspect part completeness to step on W/O	0.00
---	------

136

QC

Quality Control

Memo

0.01

DAS
38
9-89

APR 12 2016

140

Identify as per dwg & Stock Location:_____ 0.00

140

Packaging

Packaging

Memo

LOCATION: WA002

0.00

20 MIS 16-04-13

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :				MRB (QSI042) Approval 	
Description Work Order Deviation				Disposition					
								Completed By	
								Lead hand / Supervisor Approval Verification	
								QC / QA Coordinator Approval	
Root Cause		FAULT CATEGORY							
Environment ☐	No Re-verification ☐	Pressure/Forced ☐	Temperature/Cure ☐	Power Loss/Surge ☐	Positioned Wrong ☐				
Design ☐	Operator ☐	Bending ☐	Set-up ☐	Folio/Program ☐	Outside Dimensions ☐				
Doc/Data ☐	Offset/Setup ☐	Centre Not Concentric ☐	BOM/Route ☐	Grain ☐	Over/Under tolerance ☐				
Equip/Tooling ☐	Supplier ☐	Cracks ☐	Broken/Damage/Defect ☐	Weld ☐	Part Incorrect ☐				
Handling/Pre ☐	Training ☐	Crimp/Kink/Ripple/Wave ☐	Inspection Incomplete/Unqualified ☐	Wrong Stock Pulled ☐	Part Lost/Missing ☐				
Material ☐	Use for Testing ☐	Cuffs ☐	Contamination ☐	Out of Sequence ☐	Part Moved ☐				
Internal Transport ☐	Poor Information ☐	Crushing ☐	Countersink ☐	Off-set ☐	Drawing ☐				
Tribal Knowledge ☐	Rushing ☐	Heat Treat ☐	Cut Too Short ☐	Mislabeled ☐	Finish ☐				
LOA ☐	Product Improvement ☐	Wave/Twist in Tube ☐	Instructions Incomplete/Unclear ☐	Fit/Function ☐	Misread ☐				
Substation ☐	Process Improvement ☐	Marks/Chatter ☐	Drill Holes ☐	Misaligned/off center ☐	Turning Sequence ☐				
Past Expiry Date ☐	Manufacturing Process ☐	OTHER : _____							
Misidentified ☐	Past Due ☐								

Work Order ID 142660

Monday, March 21, 2016 8:40:18 AM

142660

Page 3

Item ID: D5152-1

Accept

N900040100Setup Start ***NS1***

Revision ID:

Stop ***NS2***

Item Name: Fwd Post Mount

Start Date: 3/22/2016 Start Qty: 20.00

20

Cust Item ID:

Required Date: 3/30/2016 Req'd Qty: 20.00

20

Customer:

Reference:

Approvals: Process Plan: _____ Date: _____ Tooling: _____ Date: _____

Run Start ***NR1***

QC: _____ Date: _____ SPC (Y/N): _____ Date: _____

Stop ***NR2***

Sequence ID/ Work Center ID	Operation Description	Set Up/ Run Hours	Tool ID	Tool #	Plan Code	Accept Qty	Reject Qty	Reject Number	Insp. Stamp
150	QC21- Final Inspection - Work Order Release	0.00							
150									
QC	Memo	0.03							
Quality Control									

MCS APR 13 2016

2m 16/04/13

MCS APR 13 2016

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE

QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval		
Description Work Order Deviation				Disposition				Completed By	
								Lead hand / Supervisor Approval Verification	
Root Cause Environment ☐ Design ☐ Doc/Data ☐ Equip/Tooling ☐ Handling/Pre ☐ Material ☐ Internal Transport ☐ Tribal Knowledge ☐ LOA ☐ Substation ☐ Past Expiry Date ☐ Misidentified ☐ No Re-verification ☐ Operator ☐ Offset/Setup ☐ Supplier ☐ Training ☐ Use for Testing ☐ Poor Information ☐ Rushing ☐ Product Improvement ☐ Process Improvement ☐ Manufacturing Process ☐ Past Due ☐		FAULT CATEGORY Pressure/Forced ☐ Bending ☐ Centre Not Concentric ☐ Cracks ☐ Crimp/Kink/Ripple/Wave ☐ Cuffs ☐ Crushing ☐ Heat Treat ☐ Wave/Twist in Tube ☐ Marks/Chatter ☐ Temperature/Cure ☐ Set-up ☐ BOM/Route ☐ Broken/Damage/Defect ☐ Inspection Incomplete/Unqualified ☐ Contamination ☐ Countersink ☐ Cut Too Short ☐ Instructions Incomplete/Unclear ☐ Drill Holes ☐ Power Loss/Surge ☐ Folio/Program ☐ Grain ☐ Weld ☐ Wrong Stock Pulled ☐ Out of Sequence ☐ Off-set ☐ Misabeled ☐ Fit/Function ☐ Misaligned/off center ☐ Positioned Wrong ☐ Outside Dimensions ☐ Over/Under tolerance ☐ Part Incorrect ☐ Part Lost/Missing ☐ Part Moved ☐ Drawing ☐ Finish ☐ Misread ☐ Turning Sequence ☐							
OTHER : ☐									

Picklist Print

Monday, March 21, 2016 8:40:18 AM

Page 1

Work Order ID: 142660

142660

Parent Item: D5152-1

D5152-1

Parent Item Name: Fwd Post Mount

Start Date: 3/22/2016

Required Date: 3/30/2016

Start Qty: 20.00

Required Qty: 20.00

Comments: IPP REV:A 14.09.04 NEW ISSUE DD VERF:JLM

Component Item ID/ Item Name	Replacement Item ID	Mfg/ Purch	Bin Item	Primary Location	Last Location	Route Seq ID	Unit of Measure	Qty on Hand	Qty per Kit	Total Qty	Qty Issued	Date Issued	Status
D5152-1P		Purchased	No				Each	0.0000					
D5152-1P									**	20			
Fwd Post Mount													
M304S18GA		Purchased	No				sf	269.4960		1.894736			
M304S18GA									**				
304/316 .050 Sheet													

20
20X 8016-04-7
APR 01 2016
DAS
13
9-89

Location	Loc Qty	Loc Code
MAT020	269.496	
M133328	171.996	
M133587	97.5	

m134604

DQA: _____ Date: _____



WORK ORDER NON-CONFORMANCE / UPDATE


QA Closed: _____ Date: _____

Work Order update only ☐

Work Order: _____ Part No. _____ NCR No. _____		DISPOSITION Rework ☐ Scrap ☐ Use-as-is ☐ Suspected Unapproved ☐		AGAINST DEPARTMENT/PROCESS Skid-tube ☐ Machining ☐ Thermoforming ☐ Large Fab ☐ Cross tube ☐ Small Fab ☐ Finishing ☐ Composite ☐ Water Jet ☐ Prod. Eng. Coord. ☐ Rec/Store/Packaging ☐ Supplier ☐ Engineering ☐ Quality ☐ Other ☐					
Date :		Step #:		QTY Effective :			MRB (QSI042) Approval Completed By Lead hand / Supervisor Approval Verification QC / QA Coordinator Approval		
Description Work Order Deviation				Disposition					

Root Cause				FAULT CATEGORY			
Environment ☐		No Re-verification ☐		Pressure/Forced ☐		Temperature/Cure ☐	
Design ☐		Operator ☐		Bending ☐		Set-up ☐	
Doc/Data ☐		Offset/Setup ☐		Centre Not Concentric ☐		BOM/Route ☐	
Equip/Tooling ☐		Supplier ☐		Cracks ☐		Broken/Damage/Defect ☐	
Handling/Pre ☐		Training ☐		Crimp/Kink/Ripple/Wave ☐		Inspection Incomplete/Unqualified ☐	
Material ☐		Use for Testing ☐		Cuffs ☐		Contamination ☐	
Internal Transport ☐		Poor Information ☐		Crushing ☐		Countersink ☐	
Tribal Knowledge ☐		Rushing ☐		Heat Treat ☐		Cut Too Short ☐	
LOA ☐		Product Improvement ☐		Wave/Twist in Tube ☐		Instructions Incomplete/Unclear ☐	
Substation ☐		Process Improvement ☐		Marks/Chatter ☐		Drill Holes ☐	
Past Expiry Date ☐		Manufacturing Process ☐		OTHER : _____			
Misidentified ☐		Past Due ☐					

ITEM	QTY	P/N	DESCRIPTION
	X	D5152-041	FWD POST MOUNT ASSY
1	1	D5152-1	FWD POST MOUNT
2	1	D5152-5	FWD STEP POST

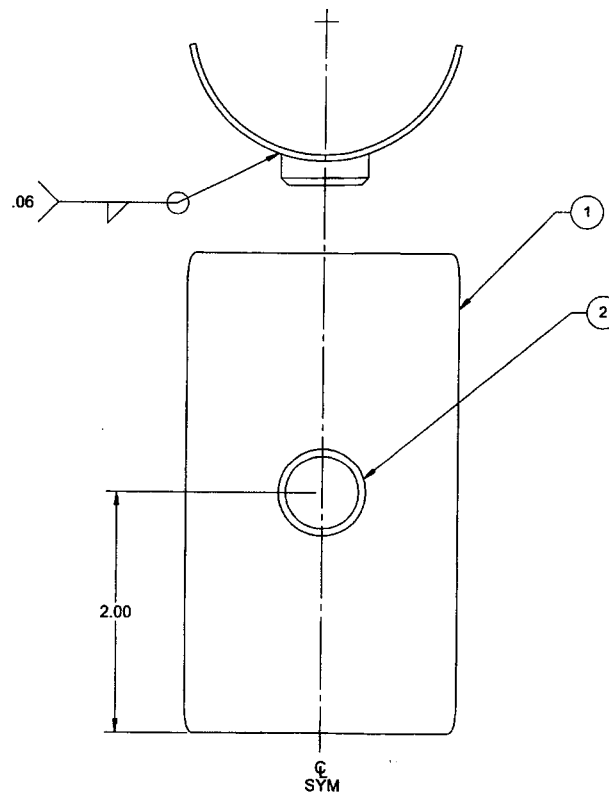

D5152-041 FWD POST MOUNT ASSEMBLY

NOTES:

- 1) MATERIAL: N/A
- 2) FINISH: PRIME PER DART QSI 005 4.2
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY PER DART QSI 044 6.1
- 7) WEIGHT: D5152-041= 0.21 lbs

SHOP COPY
RETURN TO
ENGINEERING
UNCONTROLLED COPY
SUBJECT TO AMENDMENT
WITHOUT NOTICE
WORK ORDER

NO. 142660 MLS
16-03-11

RELEASED


2015 FEB 09

ECN 15-516 4

B	COMPLETE REDESIGN, SEE PREVIOUS REV FOR DETAILS	DB	15.01.09
A	NEW ISSUE	DB	14.09.03
REV.	DESCRIPTION	BY	DATE
DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	EPDMA		
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 1 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

APPROVED

ITEM	QTY	P/N	DESCRIPTION
	X	D5152-043	AFT POST MOUNT ASSY
1	1	D5152-3	AFT POST MOUNT
2	1	D5152-7	AFT STEP POST

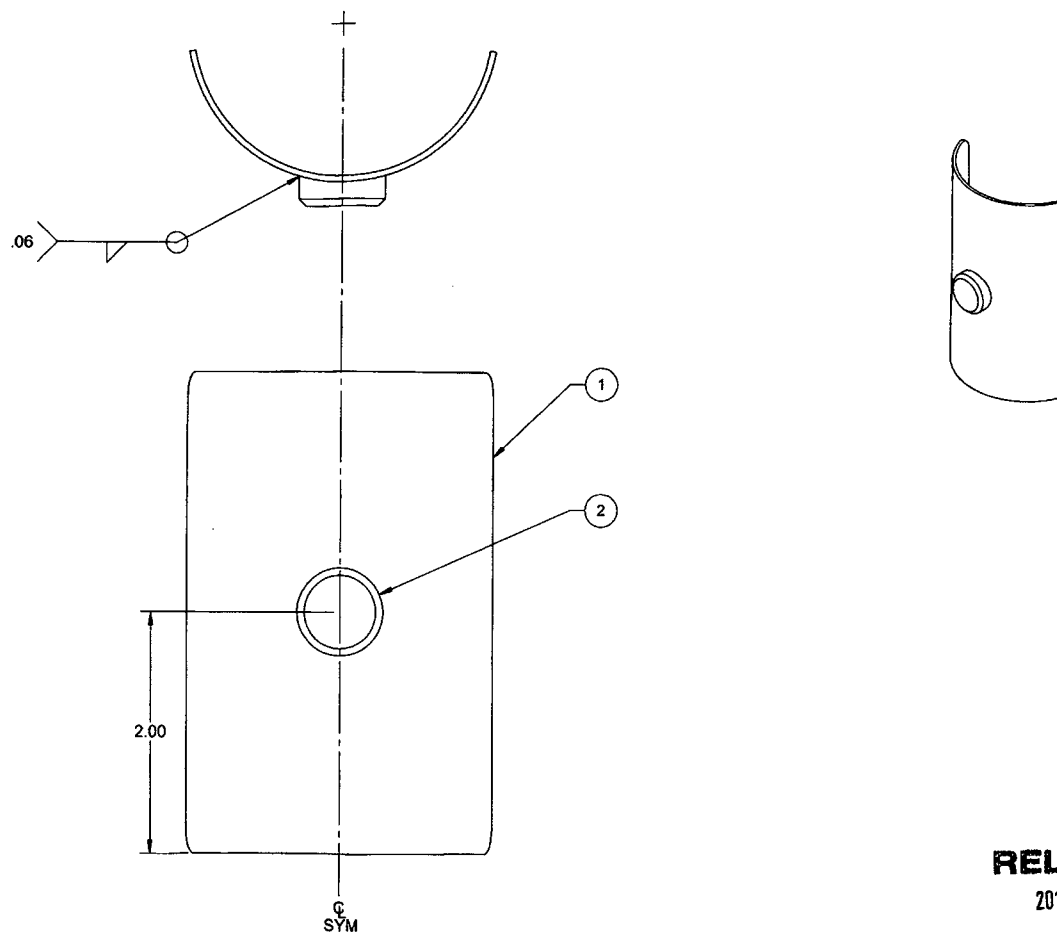

D5152-043 AFT POST MOUNT ASSEMBLY

RELEASED


2015 FEB 09

NOTES:


- 1) MATERIAL: N/A
- 2) FINISH: PRIME PER DART QSI 005 4.2
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: IDENTIFY PER DART QSI 044 6.1
- 7) WEIGHT: D5152-043= 0.23 lbs

APPROVED

DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	EPDMA		
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 2 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

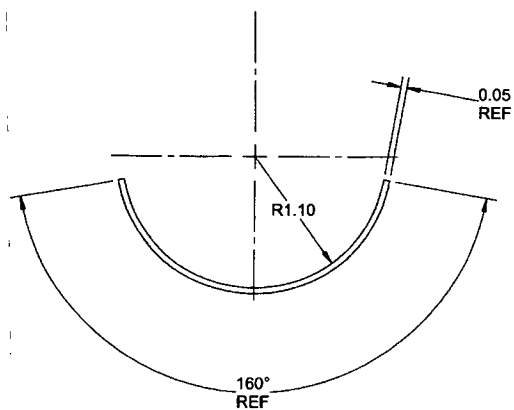

D5152-1 FWD POST MOUNT
(MAKE FROM D5152-1F)

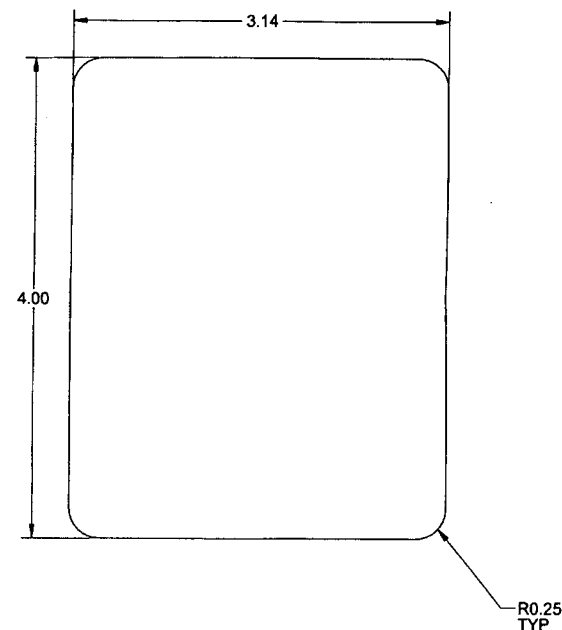

D5152-1F FWD POST MOUNT
(FLAT PATTERN)

RELEASED


2015 FEB 09

NOTES:


- 1) MATERIAL: AISI 304/316 STAINLESS STEEL SHEET PER MIL-S-5059 OR AMS 5513 OR 5524 OR ASTM A240 OR ASME SA240, 0.050" THICK (PER DART SPEC M304S18GA)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: N/A

APPROVED

DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	EPDMA		
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 3 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSES OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

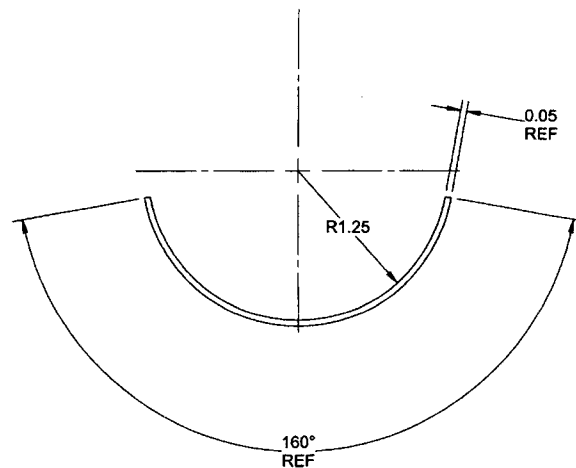

D5152-3 AFT POST MOUNT
(MAKE FROM D5152-3F)

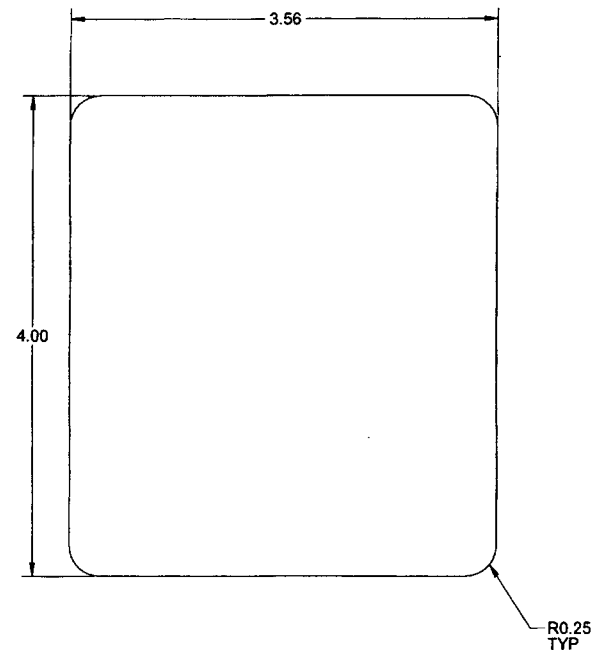

D5152-3F AFT POST MOUNT
(FLAT PATTERN)

RELEASED


2015 FEB 09

NOTES:

- 1) MATERIAL: AISI 304/316 STAINLESS STEEL SHEET PER MIL-S-5059 OR AMS 5513 OR 5524 OR ASTM A240 OR ASME SA240, 0.050" THICK (PER DART SPEC M304S18GA)
- 2) FINISH: NONE
- 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
- 4) UNITS: INCHES UNLESS OTHERWISE NOTED
- 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
- 6) IDENTIFICATION: NONE
- 7) WEIGHT: N/A

APPROVED

DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
DRAWN	EPDMA		
CHECKED	DB	DRAWING NO.	REV. B
MFG. APPR.	DD	D5152	SHEET 4 OF 5
APPROVED	HS	TITLE	SCALE
DE APPR.	DS	POST MOUNT	NTS
DATE	15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSE OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	

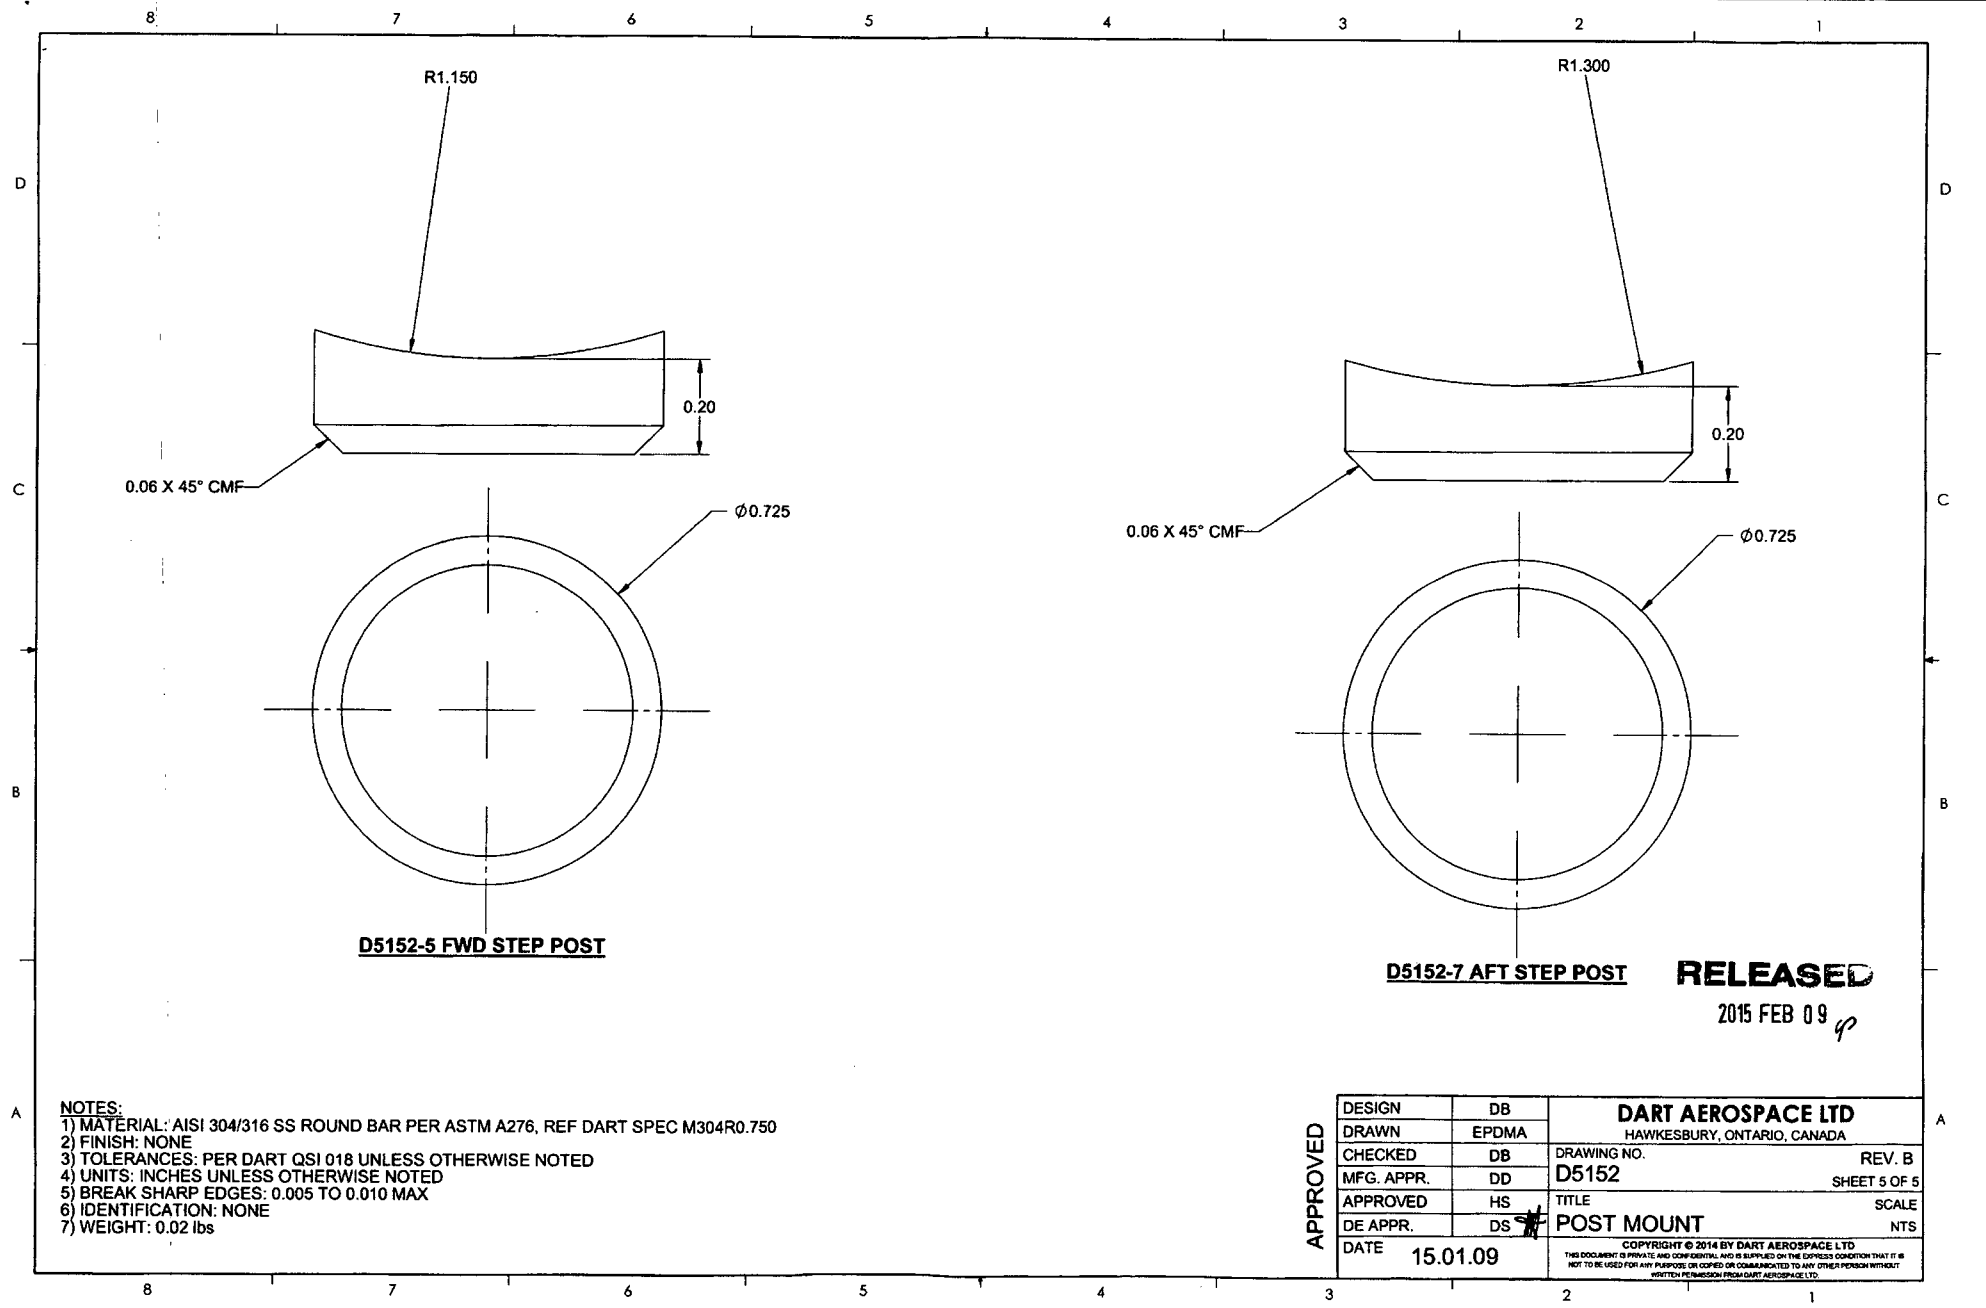

D5152-5 FWD STEP POST

D5152-7 AFT STEP POST

RELEASED

2015 FEB 09

- NOTES:**
- 1) MATERIAL: AISI 304/316 SS ROUND BAR PER ASTM A276, REF DART SPEC M304R0.750
 - 2) FINISH: NONE
 - 3) TOLERANCES: PER DART QSI 018 UNLESS OTHERWISE NOTED
 - 4) UNITS: INCHES UNLESS OTHERWISE NOTED
 - 5) BREAK SHARP EDGES: 0.005 TO 0.010 MAX
 - 6) IDENTIFICATION: NONE
 - 7) WEIGHT: 0.02 lbs

APPROVED	DESIGN	DB	DART AEROSPACE LTD HAWKESBURY, ONTARIO, CANADA	
	DRAWN	EPDMA		
	CHECKED	DB	DRAWING NO.	REV. B
	MFG. APPR.	DD	D5152	SHEET 5 OF 5
	APPROVED	HS	TITLE	SCALE
	DE APPR.	DS	POST MOUNT	NTS
DATE		15.01.09	COPYRIGHT © 2014 BY DART AEROSPACE LTD THIS DOCUMENT IS PRIVATE AND CONFIDENTIAL AND IS SUPPLIED ON THE EXPRESS CONDITION THAT IT IS NOT TO BE USED FOR ANY PURPOSES OR COPIED OR COMMUNICATED TO ANY OTHER PERSON WITHOUT WRITTEN PERMISSION FROM DART AEROSPACE LTD.	



Dart Aerospace Ltd.
1270 Aberdeen Street
Hawkesbury, ON K6A 1K7
Tel: 613 632 9577
Fax: 613 632 1053

PURCHASE ORDER
Purchase Order ID PO31764

Purchase Order Date 3/21/2016
PO Print Date 3/21/2016

Page Number 5 of 11

Order From : VC-TPI001

TPI INDUSTRIES INC.
148 RUE GOODFELLOW
DELSON, QUEBEC J5B 1V4
CANADA

Ship To : DART AEROSPACE LTD
1270 ABERDEEN
HAWKESBURY, ON K6A 1K7
CANADA

Contact Name
Vendor Phone 450-633-0484

Ship To Contact
Ship To Phone
Ship Via:
Ship Acct:

Buyer Chantal Lavoie
Customer POID
Customer Tax # 10127-2607
Terms Net 30
Currency CAD
FOB Destination-Collect

11 D4773-1P Wearplate

4/6/2016
Yes
4/6/2016

4.00
Each

\$11.75 \$47.00

CUT AS PER DWG D4773 REV. C
B143385
MATERIAL 304 SHEET 18 GA

Line Total: \$47.00

12 D5152-1P Fwd Post Mount

4/6/2016
Yes
4/6/2016

28.00
Each

\$2.25 \$63.00

CUT AS PER DWG D5152 REV. B
B142660 X 20 PCS
B143386 X 8 PCS
MATERIAL 304 SHEET 18 GA

Line Total: \$63.00

13 D2581P Mounting Bracket

4/6/2016
Yes
4/6/2016

68.00
Each

\$5.35 \$363.80

CUT AS PER DWG D2581 REV. A
B142787 X 48 PCS
B141097 X 20 PCS
MATERIAL 304 SHEET 11 GA

Note:

3/21/2016

T.P.I. INDUSTRIES INC.

148 GOODFELLOW
DELSON, QUÉBEC J5B 1V4
CANADA
Tel: (450) 633-0484
Fax: (450) 633-0879

Packing Slip

Packing Slip No.:

7443

Date:

2016-04-05

Page:

1

Sold to:		Ship to:	
Dart Aerospace Chantal Lavoie 1270 Aberdeen Hawkesbury, Ontario K6A 1K7 Canada		Dart Aerospace Chantal Lavoie 1270 Aberdeen Hawkesbury, Ontario K6A 1K7 Canada	
Order No.: 31764		Sold By: JONATHAN LESSARD	
Shipped By:		Ship Date: 2016-04-05	
Tracking No.:			

Item No.	Unit	Description	Quantity
d3805-1	Chaque	d3805-1 plate	8
d4154-1	Chaque	d4154-1 plate	8
d4406-3	Chaque	d4406-3 plate	4
d4771-1	Chaque	d4771-1 wearplate	4
d4772-1	Chaque	d4772-1 wearplate	4
d4773-1	Chaque	d4773-1 wearplate	4
d5152-1	Chaque	d5152-1 fwd post mount	28

2016-04-7

Comment: Net / 30 from date of invoice 2% svc. chg. on invoices over 30 days

THYSSENKRUPP MATERIALS NA

PART AEROSPACE

STAINLESS STEEL SHEET 304L-2B DUAL GRADE
0480 Nom X 48.0000" X 96.0000"
PART NO.

PO/Rel 31741

We certify that this is a true copy of the report
furnished by the producer of the metal, or data
resulting from tests made in approved labs.

Signed by: 

Certificate of Mill Test Results

BL PEC-983229-004

21Mar16

Pg 1/1



METALLURGICAL TEST REPORT

North American Stainless Canada Inc.
740 Imperial Road North
Guelph, ON N1K1Z3
Canada

740 Imperial Road North

Certificate: 121787 1 Mail To:
THYSSENKRUPP MATERIALS
Customer: 007206 001 2821 LANGSTAFF ROAD
CONCORD, ON L4K5C6

Ship To:
THYSSENKRUPP MATERIALS
2821 LANGSTAFF ROAD
CONCORD, ON L4K5C6

Date: 12/08/2015 Page: 1

Steel: 304/304L

Finish: 2B

Corrosion: ASTM A262/14;180Bend-OK

Your Order: PEC271093

NAS Order: WN 0072789 01

PRODUCT DESCRIPTION:

STAINLESS STEEL COIL, C.R. ANNEALED & PICKLED. UNS 30400/30403
ASTM A240/15a,A480/14b,A666/15;ASME SA240/13,SA480/13,SA666/13
CHEM ONLY ON FOLLOWING ASTM: A276/13,A479/13a,A484/13a,A312/13
CHEM ONLY ON FOLLOWING ASME: SA312/13,SA479/13
AMS 5511H/5513J XMRK; MIL-5059D AMD3(X CRN MEAS); MIL-4043B
NACE MR0175/ISO 15156-3:2009 A. MR0103/07;QSS766D-A X MAG PERM
MIN. SOLUTION ANNEAL TEMP 1900F, WATER QUENCHED

REMARKS:

Mat'l is Free of Mercury Contamination. No weld repairs.
EN 10204:2004 3.1; RoHS 1 & 2 Compliant
Material is Free of Radioactive Contamination
Steel Making Process: EAF, AOD, & Cont. Casting
Product Mfg.by a Quality Mgt.Sys. in Conf. w/ISO 9001
*Melted & Manufactured in the USA; Mat'l is DPARe Compliant

Product Id	Coil #	Skid #	Thickness	Width	Weight	-----Length-----	Mark	Pieces	Commodity Code
05X0L3 AA	05X0L3 A		.0460	48.0000	5,060	SHEETS	096.00	81	

Lab Accreditation Bureau, ISO/IEC 17025, Certificate# L2323

CHEMICAL ANALYSIS CM(Country of Melt) ES(Spain) US(United States) ZA(South Africa) JP(Japan) Chemical Analysis per ASTM A751/08


HEAT	CM	C %	CR %	CU %	MN %	MO %	N %	NI %	P %	S %
X0L3	US	.0214	18.0480	.4390	1.8095	.3690	.0812	8.0010	.0330	.0010
SI %										
.2980										

MECHANICAL PROPERTIES

Product Id#	Coil #	1 d o i c r	UTS KSI	20C .2% YS KSI	20C ELONG %-2"	% Hard RB	Tail Hard
05X0L3 AA	05X0L3 A	F T	99.26	53.12	48.68	88.00	87.00

NAS hereby certifies that the analysis on this certification is correct. Based upon the results and the accuracy
of the test methods used, the material meets the specifications stated. These results relate only to the items
tested and this report cannot be reproduced, except in its entirety, without the written approval of NAS.

Technical
Dept. Mgr.



AMHT TEST BUAVE 12/08/2015
